Printed Date/Time: 18-Nov-25 12:32 p.m.
Printed by: Diego Roisinblit

Cronoprogramma MIL08A

Name	Planned Duration
MIL08A - Construction Schedule	758d
Utilities	278d
Power	278d
HV Substation	278d
Substation Construction	278d
HV Substation Civil Works	120d
HV Substation Fitout	100d
HV Substation Testing and CX	56d
HV Substation Construction	256d
HV Line works	206d
HV Tx Install & Cx	35d
Complete Utility Power On (Commissioning Power Available)	0d
Tranche 1	417d
Phase 1 (DH1.1, PY1.1, Admin)	369d
Delivery	369d
BldgA-P1.1 Fit-Out	157d
BldgA-P1.1 L3 - L5 Commissioning	102d
Site Enabling	218d
Enabling Works / Site Cabins & UXO Survey	40d
Site Leveling	18d
Enabling & Underground Works	218d
Underground works	84d
Underground works - Below internal slab West	24d
Underground works - Below internal slab East	24d
Underground works North-West Area	40d
Underground works - Below admin slab	43d
Underground works South-West Area	40d
Underground works North-East Area	27d
Underground works South-East Area	31d
Landscaping	107d
External walls, road finishing & Landscaping	107d
Shell and Core Construction	176d
DC Shell and Core Construction	145d
Substructure	31d
Foundation DH	31d
Superstructure	147d
Internal Slabs	22d
Structural Frame - Columns and Beams DH 1&2	36d
Foundations & Slab External Yard DH1&2	36d
Roof Complete to Partial Weather tight	40d
Structural Frame - Columns and Beams DH 3&4	36d
Foundations & Slab External Yard DH3&4	36d
Roof Finishes (full Weather Tight) - Roof Gantry installation	36d
Finishes	44d

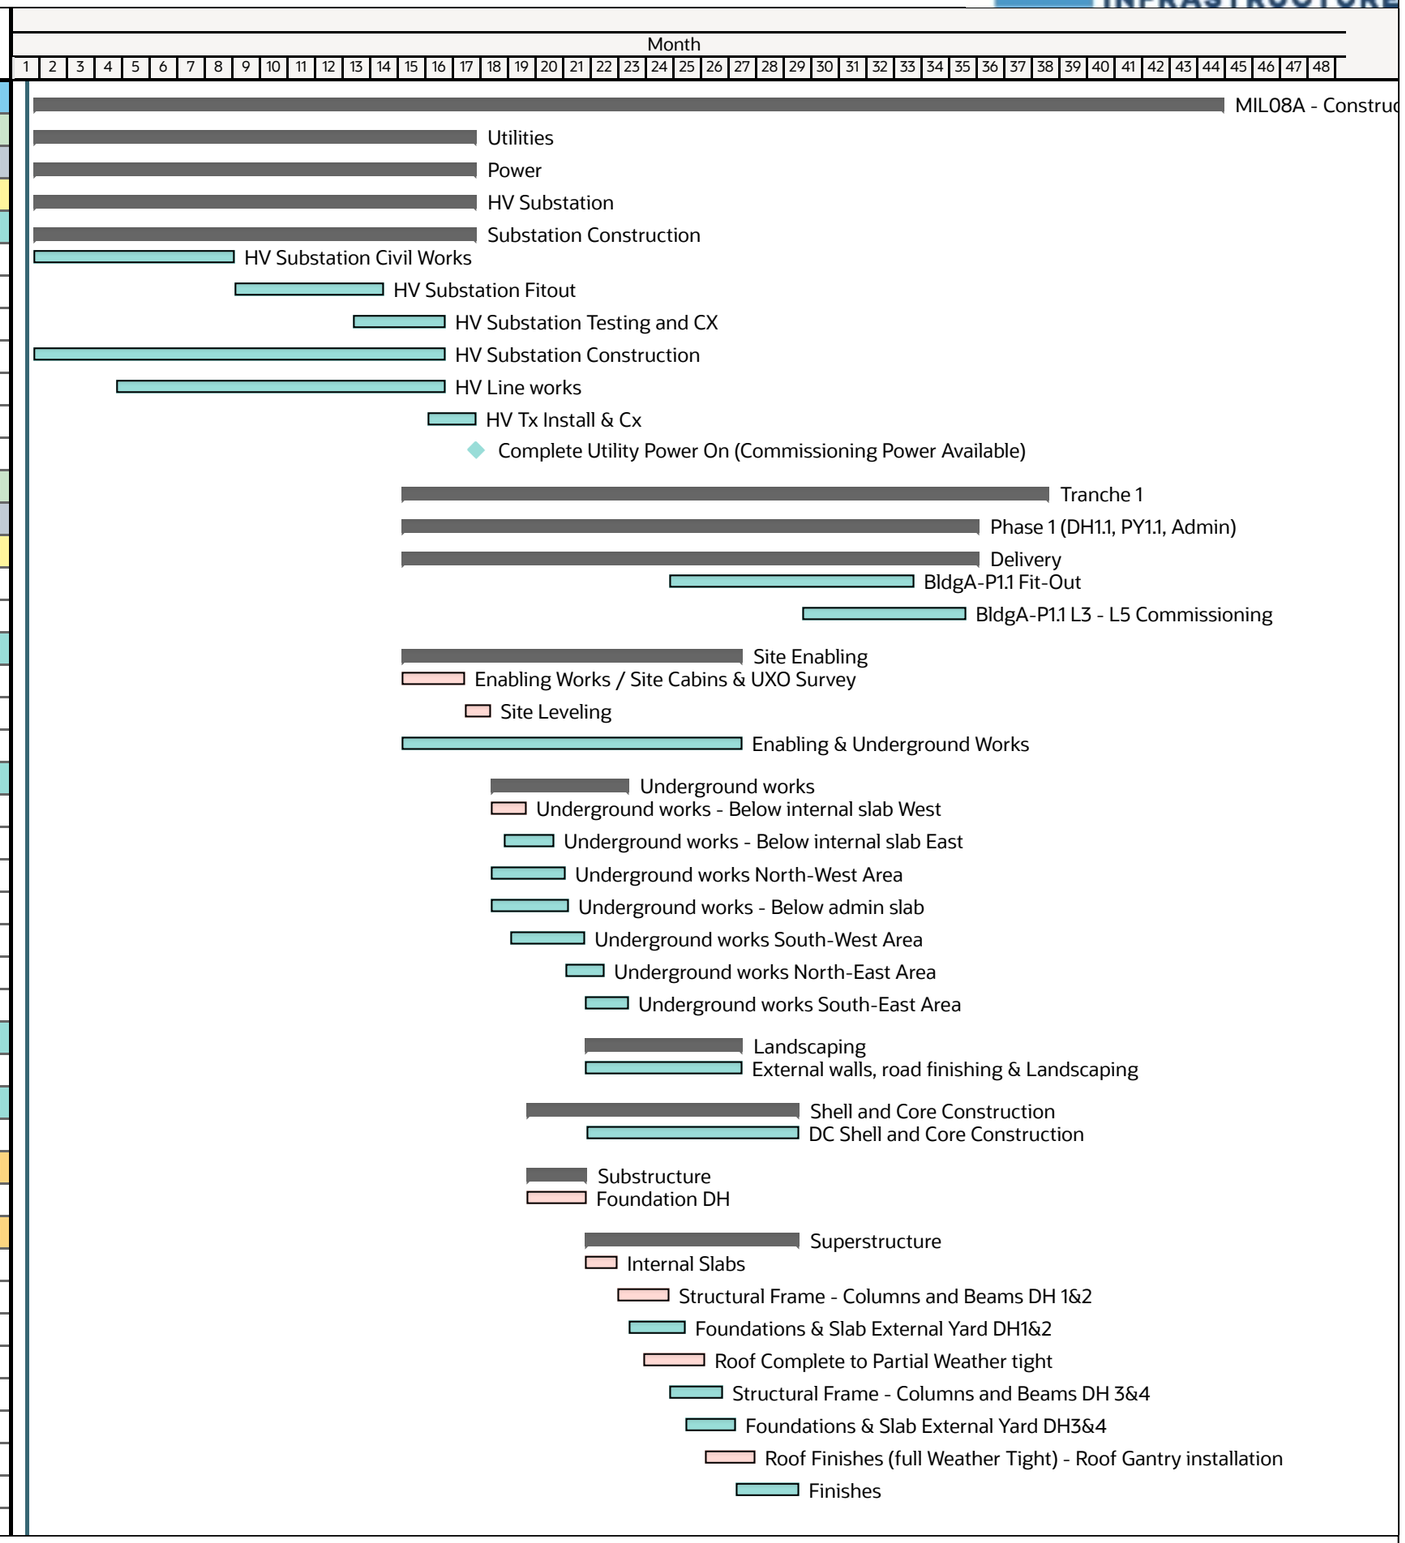

Printed Date/Time: 18-Nov-25 12:32 p.m.
Printed by: Diego Roisinblit

Cronoprogramma MIL08A

STACK INFRASTRUCTURE

Name	Planned Duration
Administration Building - Shell & Core	142d
Admin Building Shell and Core Construction	142d
Substructure	36d
Foundations - Admin	36d
Superstructure	107d
SLAB Admin	18d
Pre-cast installation Admin	40d
Admin Roof Build up	40d
Administration Building - Fitout & Commissioning	164d
Admin Building Fit Out	164d
Fit Out	107d
Install stair	9d
Loading docks	18d
Offices fit-out	89d
Plant Yard	116d
North Yard	116d
A1 - North Yard - Required on site: BldgA P1 Power modules	0d
A1 - North Yard - Gantry steel structure: BldgA P1	18d
A1 - North Yard - Required on site: BldgA P1 Generators	0d
A1 - North Yard - Installation of BldgA P1 Power modules	13d
A1 - North Yard - Installation of BldgA P1 Generators	13d
A1 - North Yard - Gantry secondary steel structure: BldgA P1	31d
A1 - North Yard - Electrical connections power modules and Sprinkler connections	40d
A1 - North Yard - Fuel connections and electrical connections generators	40d
A1 - North Yard - Installation of BldgA P1 Metal fence around plant yard	53d
A1 - North Yard - Installation of BldgA P1 Acoustic barrier	36d
A1 - North Yard - Chilled water piping system and electrical connections chillers	53d
Chillers Plant	33d
Required on site: BldgA P1 Chillers	0d
Installation of BldgA P1 Chillers	13d
Roof M&E Fit out	20d
Fit Out	157d
Datahall A1.1	157d
BldgA 1.1 Internal walls and floor installation	22d
Required on: Site internal equipment	0d
BldgA 1.1 High Level Containment	22d
BldgA 1.1 Internal Fit-out to Power on	45d
Power Required	0d
BldgA 1.1 Remaining Connections	60d
BldgA 1.1 Snagging	6d
Commissioning	102d
Level 3 Cx - Start-Up & Pre-Functional Testing	71d
BldgA-P1.1 L3 Commissioning	71d
Level 4 Cx - Functional Performance Testing	27d

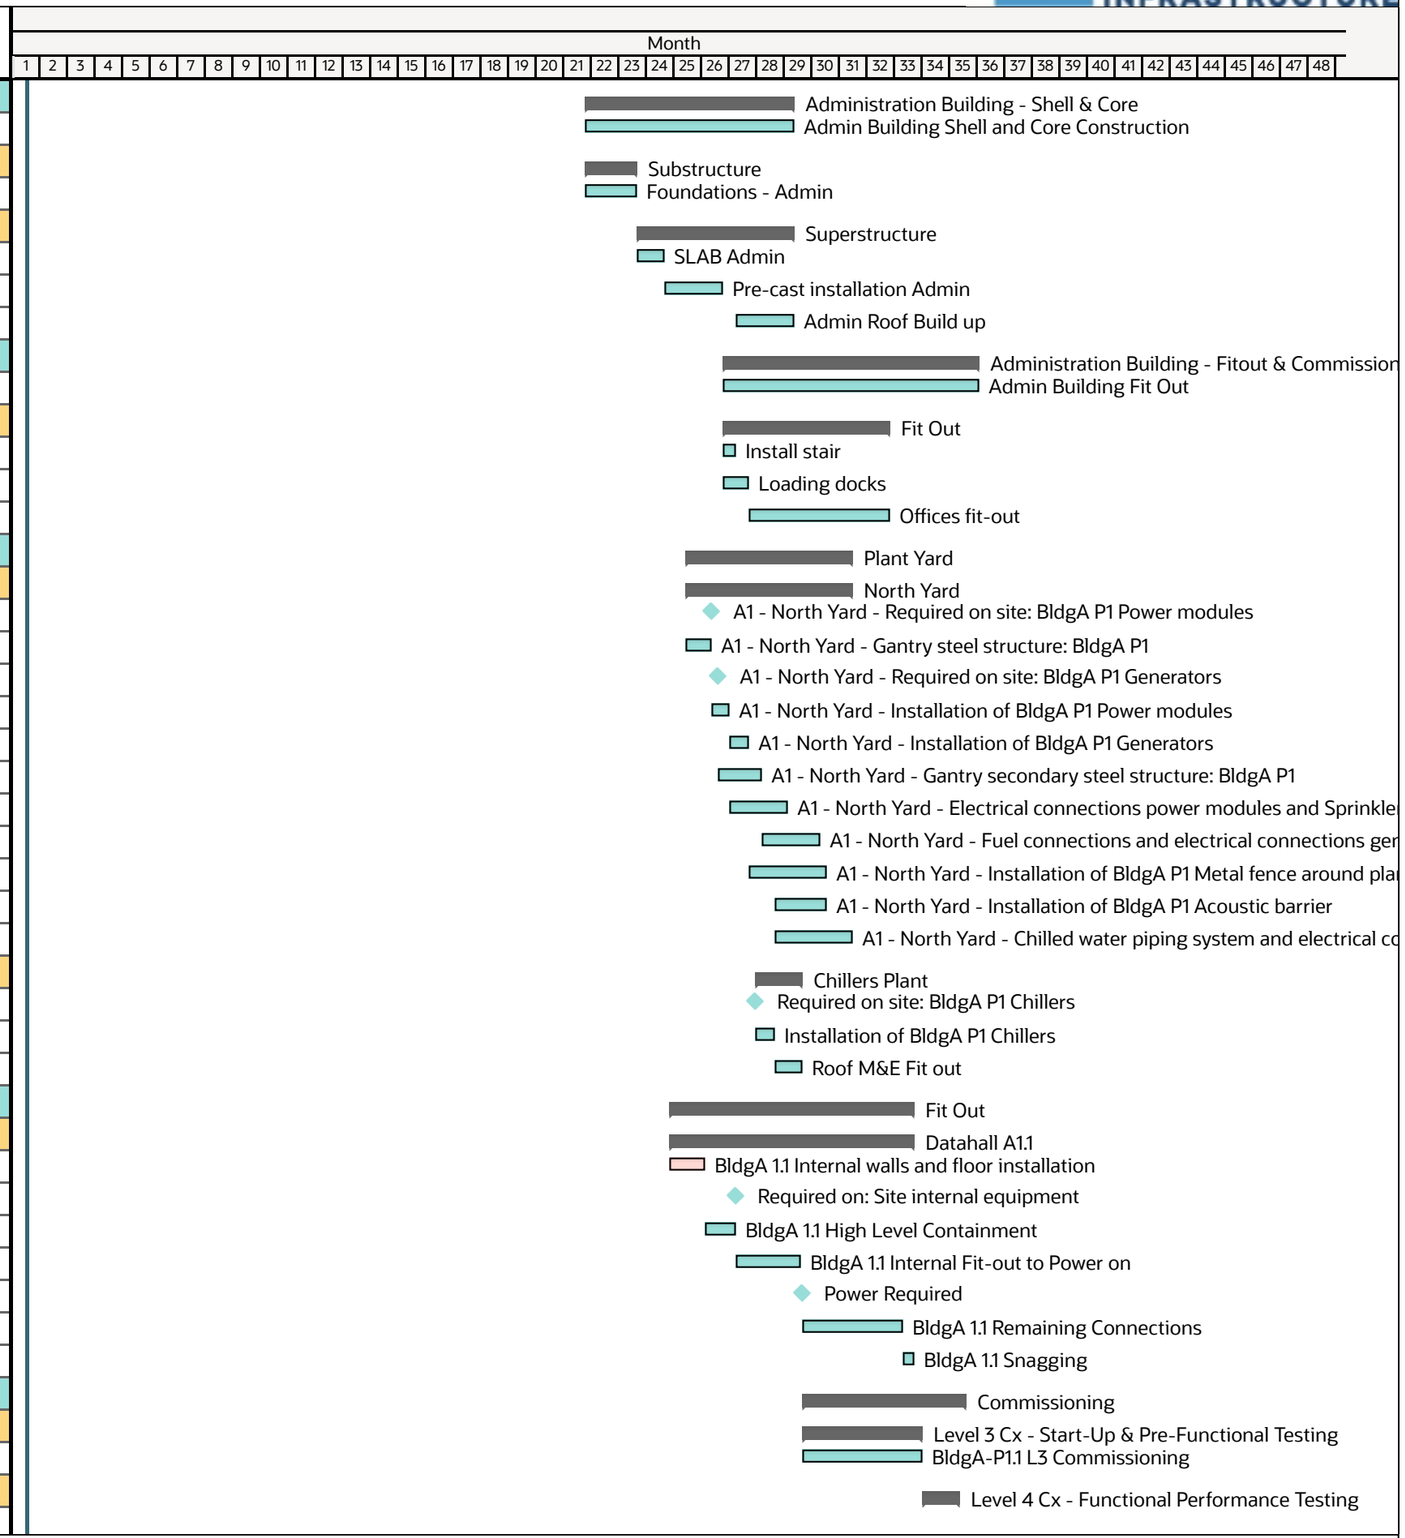

Printed Date/Time: 18-Nov-25 12:32 p.m.
Printed by: Diego Roisinblit

Cronoprogramma MIL08A

Name	Planned Duration
BldgA-P1.1 L4 Commissioning	27d
Level 5 Cx - Integrated Systems Testing	4d
BldgA-P1.1 L5 Commissioning	4d
Phase 2 (DH1.2, PY1.2)	221d
BldgA-P1.2 Fit-Out	185d
BldgA-P1.2 L3 - L5 Commissioning	102d
Delivery	221d
Plant Yard	93d
South Yard	93d
A1 - South Yard - Gantry steel structure: BldgA P1	18d
A1 - South Yard - Required on site: BldgA P1 Generators	0d
A1 - South Yard - Required on site: BldgA P1 Power modules	0d
A1 - South Yard - Installation of BldgA P1 Power modules	13d
A1 - South Yard - Installation of BldgA P1 Generators	13d
A1 - South Yard - Gantry secondary steel structure: BldgA P1	31d
A1 - South Yard - Installation of BldgA P1 Acoustic barrier	36d
A1 - South Yard - Chilled water piping system and electrical connections chillers	40d
A1 - South Yard - Electrical connections to power modules and Sprinkler connections	40d
A1 - South Yard - Installation of BldgA P1 Metal fence around plant yard	49d
A1 - South Yard - Fuel connections and electrical connections generators	44d
Fit out	159d
Datahall A1.2	159d
BldgA 1.2 Internal walls and floor installation	26d
Required on: Site internal equipment	0d
BldgA 1.2 High Level Containment	22d
Power Required	0d
BldgA 1.2 Internal Fit-out to Power on	44d
BldgA 1.2 Remaining Connections	60d
BldgA 1.2 Snagging	6d
Commissioning	102d
Level 3 Cx - Start-Up & Pre-Functional Testing	71d
BldgA-P1.2 L3 Commissioning	71d
Level 4 Cx - Functional Performance Testing	27d
BldgA-P1.2 L4 Commissioning	27d
Level 5 Cx - Integrated Systems Testing	4d
BldgA-P1.2 L5 Commissioning	4d
Tranche 2	253d
Phase 1 (DH2.1, PY2.1)	200d
Delivery	200d
BldgA2-P2.1 Fit-Out	167d
BldgA2-P2.1 L3 - L5 Commissioning	93d
Plant Yard	93d
North Yard	93d
A2 - North Yard - Required on site: BldgA P2 Power modules	0d

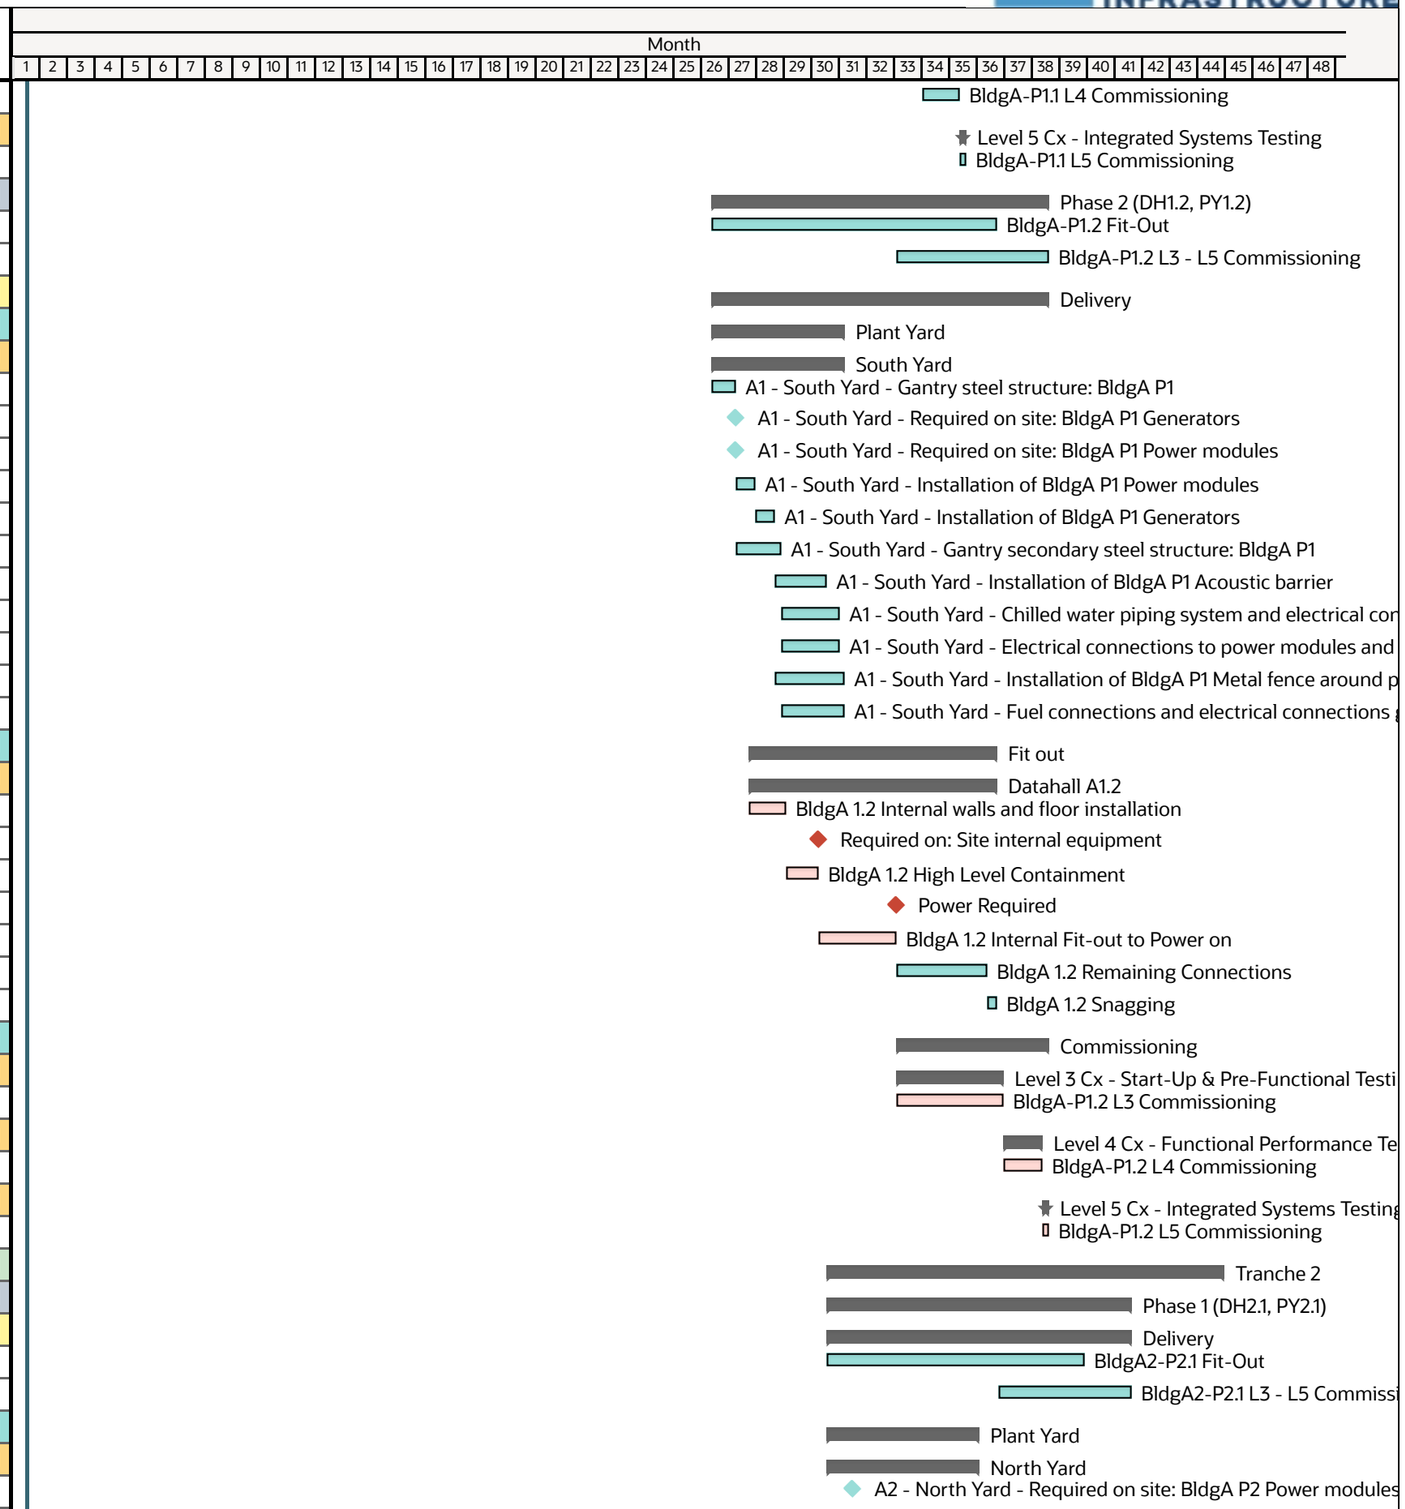

Printed Date/Time: 18-Nov-25 12:32 p.m.
Printed by: Diego Roisinblit

Cronoprogramma MIL08A

Name	Planned Duration
A2 - North Yard - Required on site: BldgA P1 Generators	0d
A2 - North Yard - Gantry steel structure: BldgA P1	18d
A2 - North Yard - Installation of BldgA P2 Power modules	13d
A2 - North Yard - Installation of BldgA P2 Generators	13d
A2 - North Yard - Chilled water piping system and electrical connections chillers	40d
A2 - North Yard - Electrical connections power modules and sprinkler connections	40d
A2 - North Yard - Gantry secondary steel structure: BldgA P2	31d
A2 - North Yard - Installation of BldgA P1 Metal fence around plant yard	36d
A2 - North Yard - Installation of BldgA P1 Acoustic barrier	36d
A2 - North Yard - Fuel connections and electrical connections generators	40d
Chillers Plant	13d
North Required on site: BldgA P2 Chillers	0d
Installation of BldgA P2 Chillers	13d
Fit Out	159d
Datahall A2.1	159d
Bldg A2.1 Internal walls and floor installation	22d
BldgA 2.1 High Level Containment	22d
Required on: Site internal equipment	0d
BldgA 2.1 Internal Fit-out to Power on	44d
Power Required	0d
BldgA 2.1 Remaining Connections	60d
BldgA 2.1 - Snagging	10d
Commissioning	93d
Level 3 Cx - Start-Up & Pre-Functional Testing	67d
BldgA-P2.1 L3 Commissioning	67d
Level 4 Cx - Functional Performance Testing	22d
BldgA-P2.1 L4 Commissioning	22d
Level 5 Cx - Integrated Systems Testing	4d
BldgA-P2.1 L5 Commissioning	4d
Phase 2 (DH2.2, PY2.2)	200d
Delivery	200d
BldgA2-P2.2 Fit-Out	191d
BldgA2-P2.2 L3 - L5 Commissioning	93d
Plant Yard	93d
South Yard	93d
A2 - South Yard - Gantry steel structure: BldgA P1	18d
A2 - South Yard - Required on site: BldgA P1 Power modules	0d
A2 - South Yard - Required on site: BldgA P1 Generators	0d
A2 - South Yard - Installation of BldgA P1 Power modules	13d
A2 - South Yard - Installation of BldgA P1 Generators	13d
A2 - South Yard - Electrical connections power modules and sprinkler connections	40d
A2 - South Yard - Gantry secondary steel structure: BldgA P1	31d
A2 - South Yard - Installation of BldgA P1 Acoustic barrier	36d
A2 - South Yard - Installation of BldgA P1 Metal fence around plant yard	36d

Printed Date/Time: 18-Nov-25 12:32 p.m.
Printed by: Diego Roisinblit

Cronoprogramma MIL08A
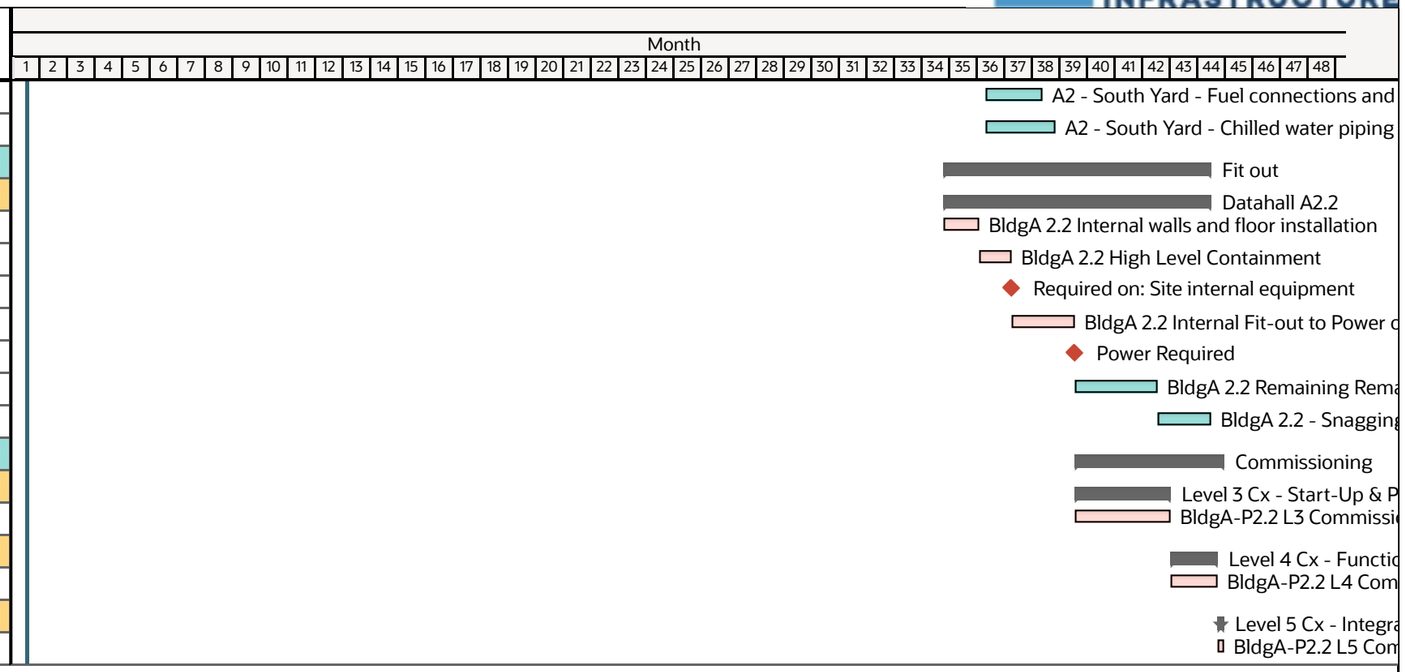
Name	Planned Duration
A2 - South Yard - Fuel connections and electrical connections generators	40d
A2 - South Yard - Chilled water piping system and electrical connections chillers	49d
Fit out	173d
Datahall A2.2	173d
BldgA 2.2 Internal walls and floor installation	22d
BldgA 2.2 High Level Containment	22d
Required on: Site internal equipment	0d
BldgA 2.2 Internal Fit-out to Power on	44d
Power Required	0d
BldgA 2.2 Remaining Remaining Connections	58d
BldgA 2.2 - Snagging	27d
Commissioning	93d
Level 3 Cx - Start-Up & Pre-Functional Testing	67d
BldgA-P2.2 L3 Commissioning	67d
Level 4 Cx - Functional Performance Testing	22d
BldgA-P2.2 L4 Commissioning	22d
Level 5 Cx - Integrated Systems Testing	4d
BldgA-P2.2 L5 Commissioning	4d
